

Assignment 2: Project Planning
Launching a Food Truck in London, Ontario

Group 03 – SOW Enterprise

Shah Masoom Kshitij (Project Manager), Adeniji Adekunle, Alain Rivera Sanchez, Himanshu
Verma

MGMT-6128-01OL-26F Project Management

Fanshawe College

[Instructor name]

October 7, 2026

Assignment 2: Project Planning – Launching a Food Truck in London, Ontario

Planning Basis

This report presents the planning deliverables for SOW Enterprise’s project to launch a food truck service in London, Ontario. It builds on the Statement of Work approved in Assignment 1, which set a 14-week window from September 8 to December 21, 2026, nine milestones, and a budget approach (Group 03, 2026a). Following the Project Management Institute’s (PMI, 2021) planning guidance, the project scope was decomposed into a work breakdown structure (WBS), the deliverables were sequenced with a precedence network, and durations were applied to produce a Gantt chart, milestone plan, and critical path.


The WBS reuses the group’s Assignment 1 activity list and interdependency analysis (Group 03, 2026b, 2026c). The 20 numbered activities from that list are retained and are cross-referenced in Table 1, so the activity numbers in the network and Gantt chart trace directly back to the earlier work.

Work Breakdown Structure

A WBS is a hierarchical decomposition of the total scope of work, and each lower level describes the work in more detail (PMI, 2019). The project WBS has three levels: the project (level 1), nine control accounts (level 2), and 22 deliverables (level 3). Every element carries a unique WBS code, and every deliverable is written as an outcome (a noun phrase) rather than an action. The 22 deliverables exceed the 20 required. Figure 1 shows the hierarchy and Table 1 is the WBS dictionary.

The WBS follows the 100% rule: the nine high-level deliverables in the Statement of Work map completely to it. Concept maps to 1.1.1, permits and approvals to 1.2, locations and events to 1.8, the purchased and fitted-out truck to 1.3 and 1.4, branding to 1.7.1, menu and pricing to 1.5.1, staffing and operating methods to 1.6, marketing and launch to 1.7.2, and the pilot and handover to 1.9 (Group 03, 2026a). Only the 22 level-3 deliverables carry durations and links; the level-1 and level-2 elements are summaries.

Figure 1
Work Breakdown Structure

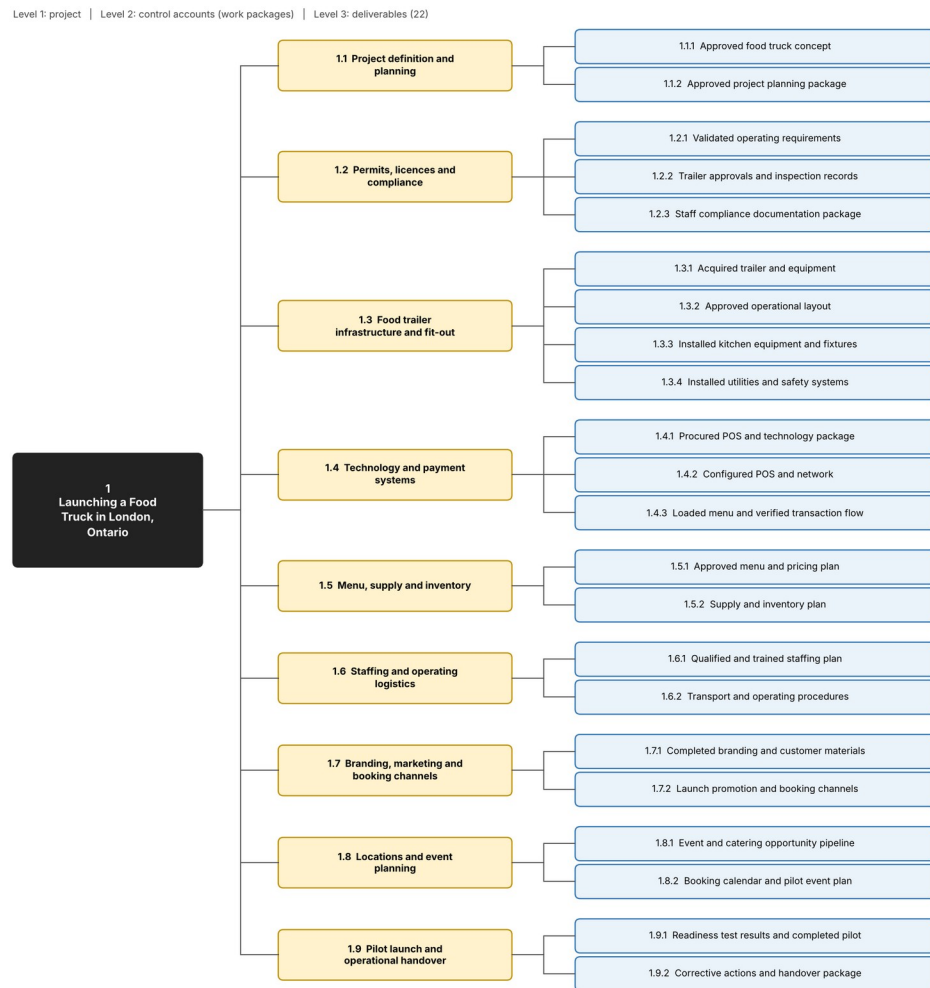

Note. Level 3 elements are the schedulable deliverables. Codes follow the Gantt chart outline in Figure 3.

Table 1
WBS Dictionary

WBS code	Deliverable	Included outputs	Source
1.1	Project definition and planning		
1.1.1	Approved food truck concept	Target customers, food offer, service style and event operating model.	SOW
1.1.2	Approved project planning package	Objectives, scope, SOW, budget baseline, schedule baseline and team responsibilities.	SOW

WBS code	Deliverable	Included outputs	Source
1.2	Permits, licences and compliance		
1.2.1	Validated operating requirements	Applicable municipal, health, fire, insurance, towing and event requirements.	Act. 1
1.2.2	Trailer approvals and inspection records	Required approvals and inspection evidence for the fitted mobile unit.	Act. 2
1.2.3	Staff compliance documentation package	Applicable certifications, safety records, coverage evidence and event documents.	Act. 3
1.3	Food trailer infrastructure and fit-out		
1.3.1	Acquired trailer and equipment	Suitable concession trailer and required cooking, refrigeration, storage and service equipment.	Act. 4
1.3.2	Approved operational layout	Kitchen workflow, equipment positions, storage, service access and safe staff movement.	Act. 5
1.3.3	Installed kitchen equipment and fixtures	Cooking and cold-holding equipment, work surfaces, sinks, shelving and service counter.	Act. 6
1.3.4	Installed utilities and safety systems	Water, wastewater, power, propane, ventilation and fire protection systems.	Act. 7
1.4	Technology and payment systems		
1.4.1	Procured POS and technology package	Required ordering and payment hardware, connectivity and software subscriptions.	Act. 8
1.4.2	Configured POS and network	Installed hardware, network connections, user access, payment settings and order routing.	Act. 9
1.4.3	Loaded menu and verified transaction flow	Menu and pricing loaded; order routing, payments, loyalty, gift cards and contingencies tested.	Act. 10
1.5	Menu, supply and inventory		
1.5.1	Approved menu and pricing plan	Food, beverages, modifiers, prices, ingredient needs and food-cost estimates.	Act. 11
1.5.2	Supply and inventory plan	Demand forecasting, supplier and restaurant production arrangements, loading quantities and inventory returns.	Act. 12
1.6	Staffing and operating logistics		
1.6.1	Qualified and trained staffing plan	Assigned roles, staffing levels, backup coverage and training in food preparation, service and payments.	Act. 13
1.6.2	Transport and operating procedures	Towing, loading, setup, opening, service, closing, teardown and return procedures.	Act. 14
1.7	Branding, marketing and booking channels		
1.7.1	Completed branding and customer materials	Exterior graphics, signage, menu displays, printed menus and event materials.	Act. 15
1.7.2	Launch promotion and booking channels	Website profile, event request form, social posts, launch announcements and booking promotion.	Act. 16

WBS code	Deliverable	Included outputs	Source
1.8	Locations and event planning		
1.8.1	Event and catering opportunity pipeline	Suitable venues, festivals, markets, private events, applications and potential partners.	Act. 17
1.8.2	Booking calendar and pilot event plan	Confirmed pilot arrangements, calendar, event requirements, inventory, staffing and transport coordination.	Act. 18
1.9	Pilot launch and operational handover		
1.9.1	Readiness test results and completed pilot	Integrated testing, readiness review, pilot service, customer feedback and issue records.	Act. 19
1.9.2	Corrective actions and handover package	Resolved issues, retesting, final procedures, lessons learned, launch approval and handover records.	Act. 20

Note. Source refers to the numbered activity in the group's activity list (Group 03, 2026b) or to the Statement of Work (SOW) phase. Outputs are drawn from the group's WBS (Group 03, 2026c).

Network Diagram

The network diagram uses the precedence diagramming method (PMI, 2021). It has one Start node, the 22 WBS deliverables, and one End node, and no node was added or removed relative to the WBS. Each node shows the WBS code, deliverable, duration, early start and finish dates, and total float; red nodes and links are the critical path. Most links are finish-to-start (FS). The “partial” dependencies identified in Assignment 1 (for example, technology procurement can begin before the layout is final) are modelled as start-to-start (SS) or finish-to-finish (FF) links with a lag in working days. Table 2 lists every link and its rationale.

Links already implied by a longer chain are omitted so the diagram stays readable; for example, 1.2.1 → 1.3.2 is implied through 1.3.1. The only deliverable without a predecessor is 1.1.1, which follows Start, and the only deliverable without a successor is 1.9.2, which leads to End; every other deliverable reaches End through 1.9.1. Milestones M1–M9 are shown as tags on the deliverable that triggers them rather than as separate nodes.

Table 2
Dependencies Between Deliverables

WBS code	Deliverable	Predecessor(s)	Rationale
1.1.1	Approved food truck concept	Start	Starting point; every other deliverable depends on an approved concept.
1.1.2	Approved project planning package	1.1.1	Scope, budget and schedule baselines require the approved concept.
1.2.1	Validated operating requirements	1.1.2	Regulatory requirements are validated against the approved plan before purchases are made.
1.3.1	Acquired trailer and equipment	1.2.1	Trailer and equipment must reflect the validated requirements.
1.3.2	Approved operational layout	1.3.1	The layout depends on the actual trailer and equipment selected.
1.3.3	Installed kitchen equipment and fixtures	1.3.2	Equipment and fixtures are installed according to the approved layout.
1.3.4	Installed utilities and safety systems	1.3.2	Utilities, propane, ventilation and fire systems follow the approved layout.
1.2.2	Trailer approvals and inspection records	1.3.3, 1.3.4	Final trailer approvals and inspections require the equipment and safety systems to be installed.
1.4.1	Procured POS and technology package	1.3.2 SS+2 d	Technology procurement can begin shortly after layout work starts (partial dependency, SS+2 d).
1.5.1	Approved menu and pricing plan	1.2.1, 1.3.1 SS+3 d	Menu follows validated requirements; it starts three days into trailer acquisition (partial dependency, SS+3 d).
1.4.2	Configured POS and network	1.3.4, 1.4.1	POS and network installation needs the technology package and electrical readiness.
1.4.3	Loaded menu and verified transaction flow	1.4.2, 1.5.1	The menu is loaded and tested only after the POS is configured and the menu is approved.
1.5.2	Supply and inventory plan	1.5.1	Supply and inventory planning depends on the approved menu.
1.6.2	Transport and operating procedures	1.3.2, 1.3.3 FF, 1.3.4 FF	Procedures are drafted once the layout is approved and finalised when installation finishes (FF).
1.6.1	Qualified and trained staffing plan	1.5.1, 1.6.2 SS+3 d	Staffing follows the approved menu and starts three days into procedure development (SS+3 d).
1.2.3	Staff compliance documentation package	1.6.1 SS+5 d	Compliance documents are verified as staffing profiles take shape (SS+5 d).
1.7.1	Completed branding and customer materials	1.3.2, 1.5.1 FF	Branding needs the approved layout (service windows) and cannot finish before the menu display content (FF).
1.7.2	Launch promotion and booking channels	1.7.1	Promotion and booking channels reflect the finished branding.
1.8.1	Event and catering opportunity pipeline	1.2.1	Commercial outreach starts once operating requirements and constraints are validated.

WBS code	Deliverable	Predecessor(s)	Rationale
1.8.2	Booking calendar and pilot event plan	1.5.2, 1.6.1, 1.6.2, 1.8.1	The event calendar needs the supply, staffing, logistics and opportunity-pipeline plans.
1.9.1	Readiness test results and completed pilot	1.2.2, 1.2.3, 1.4.3, 1.7.2, 1.8.2	The pilot is the integration point: infrastructure, compliance, POS, staffing, marketing and events must be ready.
1.9.2	Corrective actions and handover package	1.9.1	Handover follows pilot results, corrective actions and retesting.


Note. FS links have no suffix; SS = start-to-start; FF = finish-to-finish; +n d = lag in working days. Shaded rows are on the critical path. After handover, the recurring event cycle (opportunity, booking, forecast, staffing, logistics, operation, teardown, review) described in Group 03 (2026b) continues as operations and is outside this project network.

Gantt Chart and Milestones

Figure 3
Gantt Chart With Milestones and Critical Path

Food Truck Launch - London, Ontario | SOW Enterprise (Group 03) | Gantt chart, Sep 8 - Dec 21, 2026

Working calendar: Mon-Fri, 8 h/day; Oct 12 (Thanksgiving) non-working. Links: FS unless marked (SS = start-to-start, FF = finish-to-finish; +n = lag in working days).

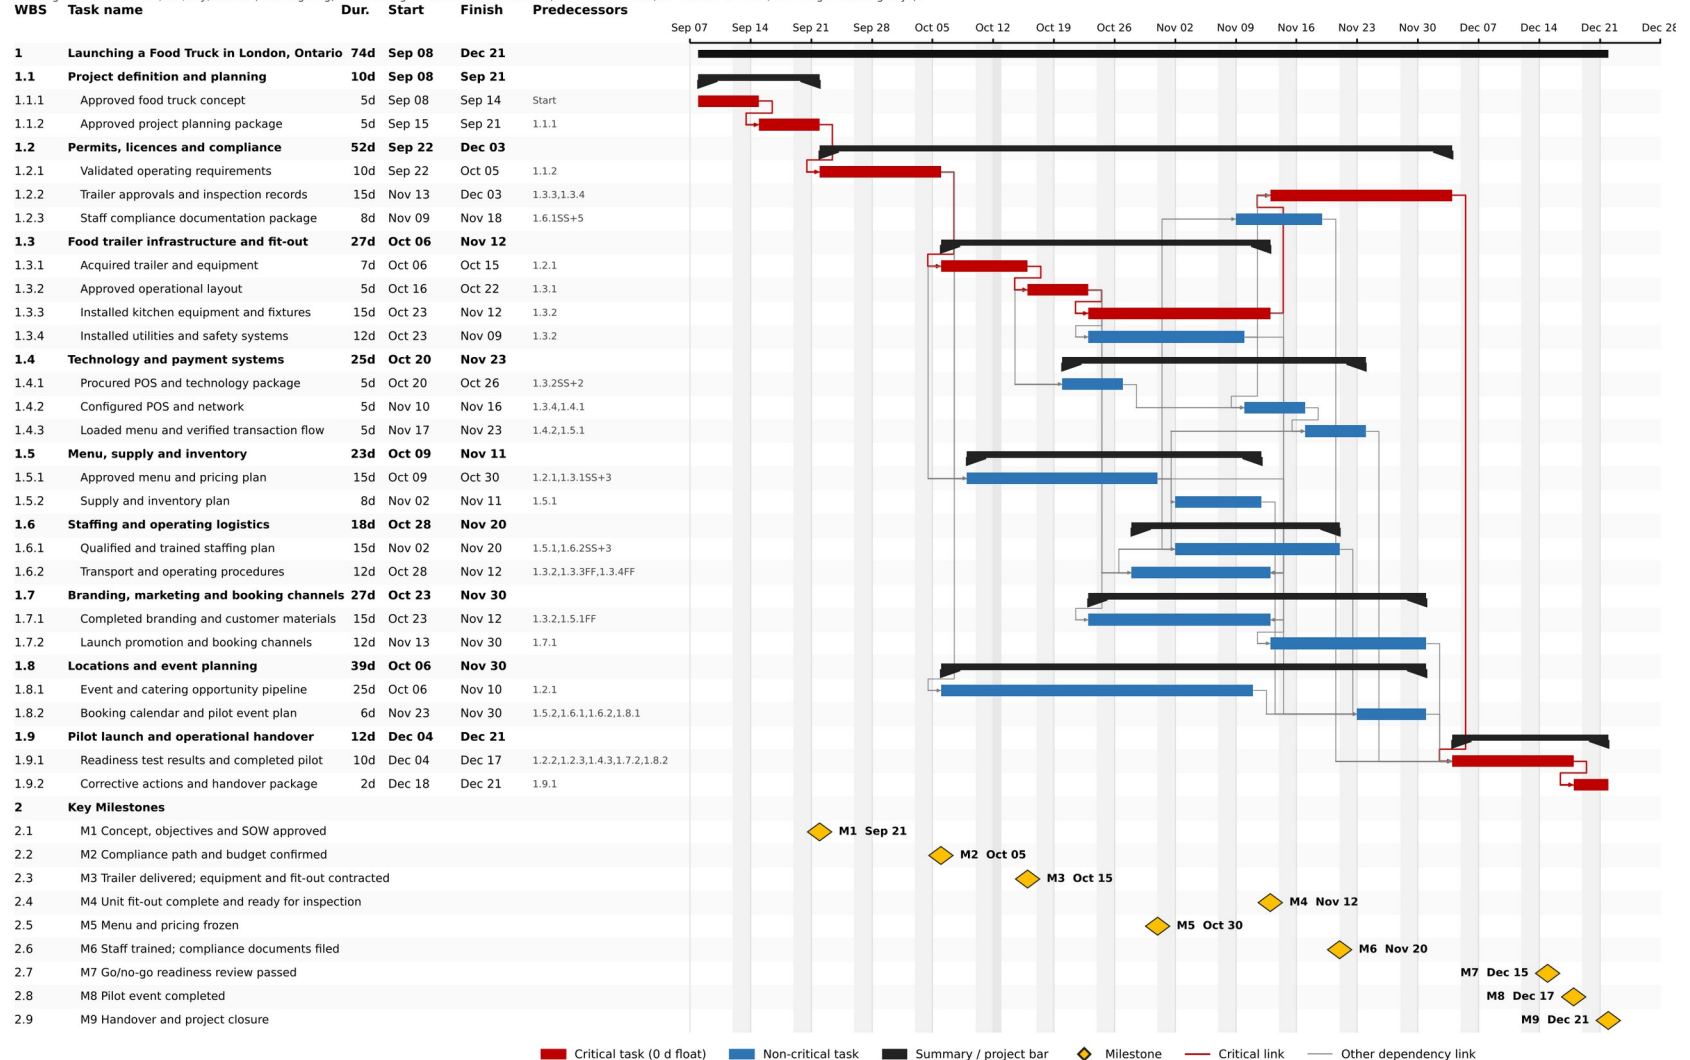

Note. Red bars are critical tasks (0 days of total float); diamonds are milestones M1–M9. The schedule is provided as the Microsoft Project file Food_Truck_Project_Plan.xml submitted with this report.

The schedule is built on a Monday-to-Friday, 8-hour working calendar that treats Thanksgiving Day (October 12, 2026) as non-working. All 22 deliverables are scheduled with the links in Table 2, and the nine control accounts roll up as summary tasks. Durations are working days estimated by the team from the Assignment 1 phase plan, the scope of each deliverable, and the third-party lead times (municipal, health, fire, TSSA, and ESA approvals) that Assignment 1 assumed would be obtained within the schedule (Group 03, 2026a). The plan starts on September 8, 2026 and finishes on December 21, 2026, a total of 74 working days (14 weeks).

Nine milestones mark the decision gates (Table 4). Milestones have zero duration and are linked to the deliverable that triggers them; M7 (go/no-go review) is placed seven working days into the readiness-and-pilot deliverable 1.9.1, because the readiness review is part of that deliverable's outputs. Table 3 gives the full schedule.

Table 3
Schedule of Deliverables

WBS	Deliverable	Act.	Dur.	Start	Finish	Predecessor(s)	Total float	Critical
1.1.1	Approved food truck concept	SOW	5 d	Sep 8, 2026	Sep 14, 2026	Start	0 d	Yes
1.1.2	Approved project planning package	SOW	5 d	Sep 15, 2026	Sep 21, 2026	1.1.1	0 d	Yes
1.2.1	Validated operating requirements	1	10 d	Sep 22, 2026	Oct 5, 2026	1.1.2	0 d	Yes
1.2.2	Trailer approvals and inspection records	2	15 d	Nov 13, 2026	Dec 3, 2026	1.3.3, 1.3.4	0 d	Yes
1.2.3	Staff compliance documentation package	3	8 d	Nov 9, 2026	Nov 18, 2026	1.6.1 SS+5 d	11 d	No
1.3.1	Acquired trailer and equipment	4	7 d	Oct 6, 2026	Oct 15, 2026	1.2.1	0 d	Yes
1.3.2	Approved operational layout	5	5 d	Oct 16, 2026	Oct 22, 2026	1.3.1	0 d	Yes
1.3.3	Installed kitchen equipment and fixtures	6	15 d	Oct 23, 2026	Nov 12, 2026	1.3.2	0 d	Yes
1.3.4	Installed utilities and safety systems	7	12 d	Oct 23, 2026	Nov 9, 2026	1.3.2	3 d	No
1.4.1	Procured POS and technology package	8	5 d	Oct 20, 2026	Oct 26, 2026	1.3.2 SS+2 d	18 d	No
1.4.2	Configured POS and network	9	5 d	Nov 10, 2026	Nov 16, 2026	1.3.4, 1.4.1	8 d	No
1.4.3	Loaded menu and verified transaction flow	10	5 d	Nov 17, 2026	Nov 23, 2026	1.4.2, 1.5.1	8 d	No
1.5.1	Approved menu and pricing plan	11	15 d	Oct 9, 2026	Oct 30, 2026	1.2.1, 1.3.1 SS+3 d	3 d	No
1.5.2	Supply and inventory plan	12	8 d	Nov 2, 2026	Nov 11, 2026	1.5.1	10 d	No
1.6.1	Qualified and trained staffing plan	13	15 d	Nov 2, 2026	Nov 20, 2026	1.5.1, 1.6.2 SS+3 d	3 d	No

WBS	Deliverable	Act.	Dur.	Start	Finish	Predecessor(s)	Total float	Critical
1.6.2	Transport and operating procedures	14	12 d	Oct 28, 2026	Nov 12, 2026	1.3.2, 1.3.3 FF, 1.3.4 FF	3 d	No
1.7.1	Completed branding and customer materials	15	15 d	Oct 23, 2026	Nov 12, 2026	1.3.2, 1.5.1 FF	3 d	No
1.7.2	Launch promotion and booking channels	16	12 d	Nov 13, 2026	Nov 30, 2026	1.7.1	3 d	No
1.8.1	Event and catering opportunity pipeline	17	25 d	Oct 6, 2026	Nov 10, 2026	1.2.1	11 d	No
1.8.2	Booking calendar and pilot event plan	18	6 d	Nov 23, 2026	Nov 30, 2026	1.5.2, 1.6.1, 1.6.2, 1.8.1	3 d	No
1.9.1	Readiness test results and completed pilot	19	10 d	Dec 4, 2026	Dec 17, 2026	1.2.2, 1.2.3, 1.4.3, 1.7.2, 1.8.2	0 d	Yes
1.9.2	Corrective actions and handover package	20	2 d	Dec 18, 2026	Dec 21, 2026	1.9.1	0 d	Yes

Note. Dur. = duration in working days. Total float is the number of working days a deliverable can slip without delaying the December 21, 2026 finish. Shaded rows are critical.

Table 4*Milestones: Assignment 1 Targets Compared With the Scheduled Plan*

ID	Milestone	Triggered by	Assignment 1 target	Scheduled	Variance (calendar days)
M1	Concept, objectives and SOW approved	1.1.2	Sep 21, 2026	Sep 21, 2026	0 d
M2	Compliance path and budget confirmed	1.2.1	Oct 5, 2026	Oct 5, 2026	0 d
M3	Trailer delivered; equipment and fit-out contracted	1.3.1	Oct 15, 2026	Oct 15, 2026	0 d
M4	Unit fit-out complete and ready for inspection	1.3.3, 1.3.4	Nov 5, 2026	Nov 12, 2026	+7 d
M5	Menu and pricing frozen	1.5.1	Nov 15, 2026	Oct 30, 2026	-16 d
M6	Staff trained; compliance documents filed	1.6.1, 1.2.3	Nov 23, 2026	Nov 20, 2026	-3 d
M7	Go/no-go readiness review passed	1.9.1 SS+7 d	Dec 15, 2026	Dec 15, 2026	0 d
M8	Pilot event completed	1.9.1	Dec 18, 2026	Dec 17, 2026	-1 d
M9	Handover and project closure	1.9.2	Dec 21, 2026	Dec 21, 2026	0 d

Note. M1, M2, M3, M7, and M9 match the Assignment 1 targets. Triggered by lists the WBS deliverable(s) whose completion drives the milestone.

Four milestone dates differ from the Assignment 1 estimates because the dependency analysis gave a more detailed sequence. M4 moves seven days later because the fit-out of the kitchen equipment (1.3.3) takes 15 working days after the layout is approved. M5 moves 16 days earlier because the menu (1.5.1) can start as soon as operating requirements are validated, while the standard operating procedures are finalised later in 1.6.2. M6 is three days earlier and M8 one day earlier. Because the Project Sponsor approved the Assignment 1 dates as targets, these four changes should be recorded through the project's change-control process (Group 03, 2026a).

Critical Path

The critical path is the longest sequence of dependent deliverables and therefore determines the earliest possible finish date (Kelley & Walker, 1959; PMI, 2021). The path, highlighted in red in Figures 2 and 3, is 1.1.1 → 1.1.2 → 1.2.1 → 1.3.1 → 1.3.2 → 1.3.3 → 1.2.2 → 1.9.1 → 1.9.2. Its nine deliverables add up to 74 working days, so every day of delay on any of them delays the December 21, 2026 handover by a day (Table 5).

Table 5
Critical Path Deliverables

Seq.	WBS	Deliverable	Duration	Start	Finish
1	1.1.1	Approved food truck concept	5 d	Sep 8, 2026	Sep 14, 2026
2	1.1.2	Approved project planning package	5 d	Sep 15, 2026	Sep 21, 2026
3	1.2.1	Validated operating requirements	10 d	Sep 22, 2026	Oct 5, 2026
4	1.3.1	Acquired trailer and equipment	7 d	Oct 6, 2026	Oct 15, 2026
5	1.3.2	Approved operational layout	5 d	Oct 16, 2026	Oct 22, 2026
6	1.3.3	Installed kitchen equipment and fixtures	15 d	Oct 23, 2026	Nov 12, 2026
7	1.2.2	Trailer approvals and inspection records	15 d	Nov 13, 2026	Dec 3, 2026
8	1.9.1	Readiness test results and completed pilot	10 d	Dec 4, 2026	Dec 17, 2026
9	1.9.2	Corrective actions and handover package	2 d	Dec 18, 2026	Dec 21, 2026
		Total critical path duration	74 d	Sep 8, 2026	Dec 21, 2026

Note. Durations are working days. The path is driven by the physical trailer chain (acquisition, layout, kitchen installation) followed by the final trailer approvals and inspections.

Schedule Implications

The plan has no schedule reserve on the critical path. The longest and least controllable activity on it is 1.2.2, trailer approvals and inspections (15 working days), which depends on external inspectors. The team can protect the date by booking inspection slots early while 1.3.3 is under way, by asking contractors to pre-inspect the installation, and by splitting the approvals so that fire, electrical, propane, and health inspections run in parallel (fast tracking). If the date is still at risk, adding installation crew to 1.3.3 would shorten it (crashing) at the cost of the contingency in the Assignment 1 budget (Group 03, 2026a; PMI, 2021).

A second chain is almost as long: menu and pricing (1.5.1) → staffing and training (1.6.1) → booking calendar (1.8.2) → pilot (1.9.1) has three working days of float, as do utilities installation (1.3.4), procedures (1.6.2), and branding and promotion (1.7.1 and 1.7.2). These near-critical deliverables should be reported with the same attention as the critical path. The Project Manager should review progress weekly and report any slip on these chains to the Sponsor.

AI Use Disclosure

An AI assistant (Claude, Anthropic) was used to apply critical path calculations to the group's activity list, generate the diagrams and the Microsoft Project file, and draft text. The activities, dependencies, and project context come from the group's Assignment 1 work, and the team reviewed the content before submission.

References

- Group 03. (2026a). *Assignment 1: SOW Enterprise – statement of work for launching a food truck in London, Ontario* [Unpublished course assignment]. MGMT-6128, Fanshawe College.
- Group 03. (2026b). *Food truck project activities and interdependencies* [Unpublished course document]. MGMT-6128, Fanshawe College.
- Group 03. (2026c). *Food truck project work breakdown structure* [Unpublished course document]. MGMT-6128, Fanshawe College.
- Kelley, J. E., Jr., & Walker, M. R. (1959). Critical-path planning and scheduling. In *Papers presented at the December 1–3, 1959, Eastern Joint IRE-AIEE-ACM Computer Conference* (pp. 160–173). Association for Computing Machinery.
<https://doi.org/10.1145/1460299.1460318>
- Project Management Institute. (2019). *Practice standard for work breakdown structures* (3rd ed.). Author.
- Project Management Institute. (2021). *A guide to the project management body of knowledge (PMBOK® guide)* (7th ed.). Author.
